


	📅	Name	Duration	Start	Finish	Predecessors	Resource Names	28 Nov 21						
								S	M	T	W	T		
1	📅	Gunning	0 days	12/1/21 8:30 AM	12/1/21 8:30 AM									
2		<b>Fase 1: doorgronden o...</b>	<b>45 days?</b>	<b>12/1/21 8:30 AM</b>	<b>2/11/22 8:30 AM</b>									
3	📅	Startoverleg	0 days	12/13/21 8:30 AM	12/13/21 8:30 AM									
4		Verlag startoverleg	1 day?	12/13/21 8:30 AM	12/14/21 8:30 AM									
5		Veldbezoek	1 day?	12/15/21 8:30 AM	12/16/21 8:30 AM									
6		Verlag veldbezoek	11.938 days?	12/16/21 8:30 AM	1/11/22 5:00 PM									
7		MS project planning	2 days?	1/3/22 8:30 AM	1/5/22 8:30 AM	3								
8		<b>Ontvangen gegevens</b>	<b>18 days?</b>	<b>12/1/21 8:30 AM</b>	<b>12/30/21 8:30 AM</b>									
9		Ontvangen onderzoek ...	1 day?	12/10/21 8:30 AM	12/13/21 8:30 AM									
10		Ontvangen bodemche...	21 days?	12/1/21 8:30 AM	12/30/21 8:30 AM	1					Prolander			
11		Ontvangen hydrobiolo...	21 days?	12/1/21 8:30 AM	12/30/21 8:30 AM	1					Prolander			
12	✅	Ontvangen onderzoek ...	1 day?	12/13/21 8:30 AM	12/14/21 8:30 AM	1					Prolander			
13		Samenvatten onderzoeken	1 day?	12/30/21 8:30 AM	12/31/21 8:30 AM	10;11;12;9								
14		aanleveren welke percel...	1 day?	12/30/21 8:30 AM	12/31/21 8:30 AM	8								
15	📅	toestemming veldwerk	7 days	1/11/22 8:30 AM	1/20/22 8:30 AM	14					Prolander			
16		Veldwerk	2 days	1/20/22 8:30 AM	1/24/22 8:30 AM	8;15								
17		Plannen overleg grondei...	1 day?	12/13/21 8:30 AM	12/14/21 8:30 AM	3					Prolander			
18		Overleg grondeigenaren	14 days?	12/30/21 8:30 AM	1/25/22 8:30 AM	10;11;12								
19		Inplannen werksessie	14 days	12/30/21 8:30 AM	1/25/22 8:30 AM	8								
20		Werksessie Concretisere...	1 day?	1/25/22 8:30 AM	1/26/22 8:30 AM	3;5;19;13;16					Prolander: inhoudelijke input			
21		Opstellen Notitie kansrijk...	10 days	1/26/22 8:30 AM	2/9/22 8:30 AM	20								
22		notitie kansrijke maatreg...	1 day?	2/9/22 8:30 AM	2/10/22 8:30 AM	21								
23		Opstellen Inhoudsopgav...	10 days	1/26/22 8:30 AM	2/9/22 8:30 AM	20								
24		inhoudsopgave concept	1 day?	2/9/22 8:30 AM	2/10/22 8:30 AM	23								
25		Afrondende sessie result...	1 day?	2/10/22 8:30 AM	2/11/22 8:30 AM	21;24								
26		<b>Fase 2: uitvoerbaar ont...</b>	<b>90 days?</b>	<b>1/25/22 8:30 AM</b>	<b>6/10/22 8:30 AM</b>									
27	📅	Startoverleg fase 2	5 days?	2/11/22 8:30 AM	2/18/22 8:30 AM	25								
28	📅	Inplannen brede werkse...	21 days	1/25/22 8:30 AM	2/23/22 8:30 AM	18					Prolander			





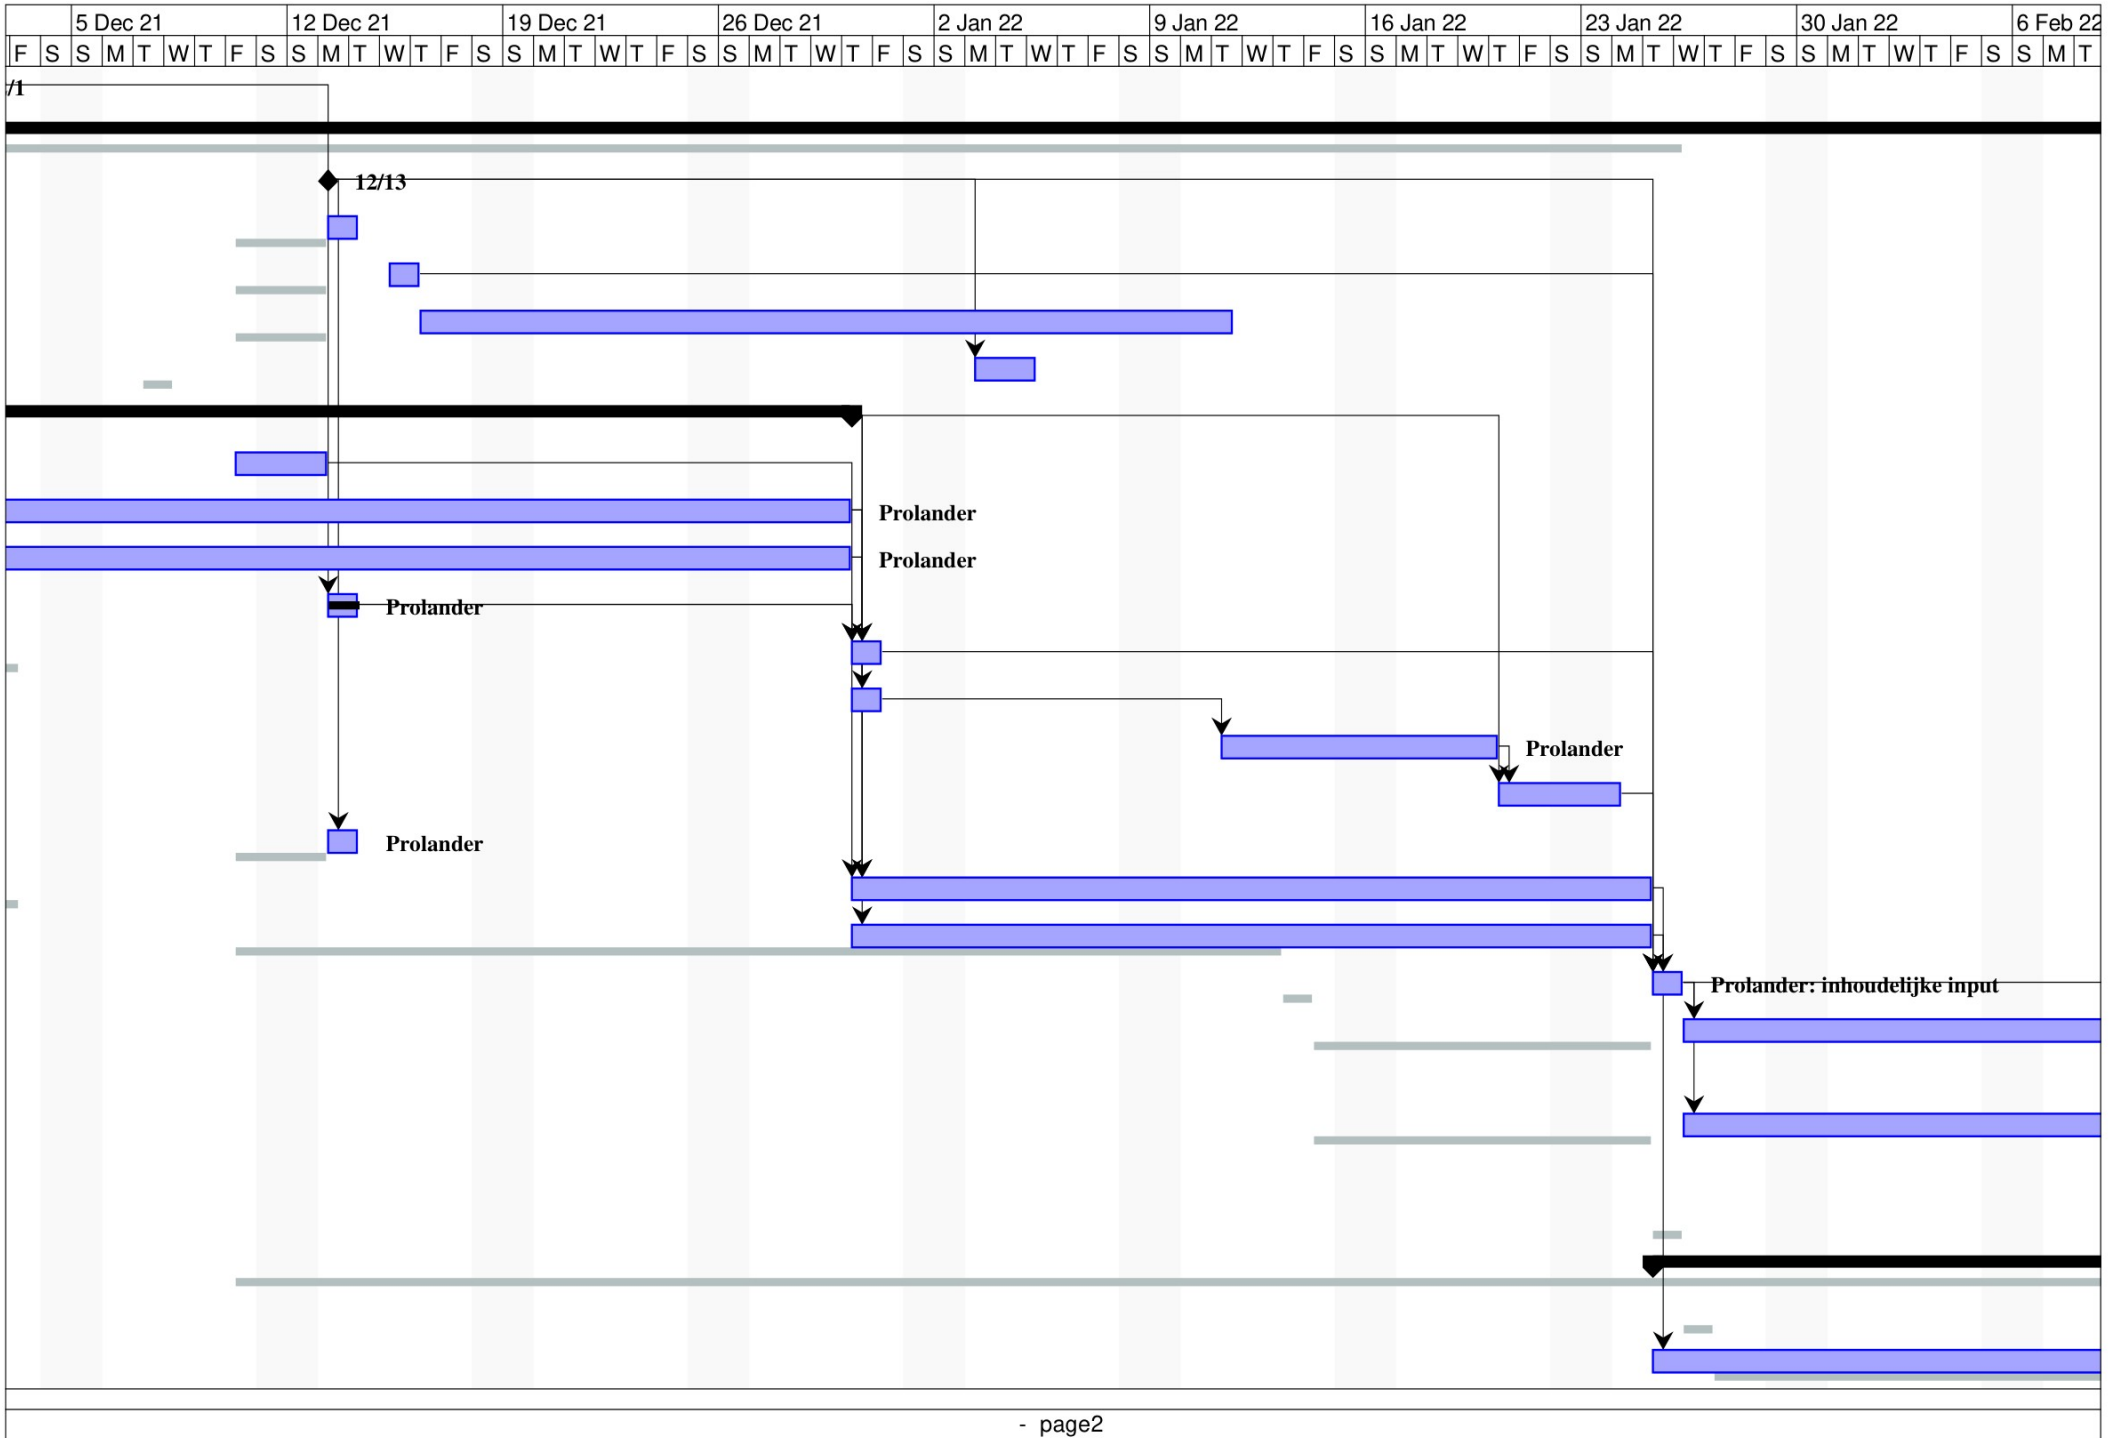


Apr 22					24 Apr 22					1 May 22					8 May 22					15 May 22					22 May 22					29 May 22					5 Jun 22					12 Jun 22					19 Jun 22																
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S









7 22				13 Nov 22				20 Nov 22				27 Nov 22				4 Dec 22				11						
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

		Name	Duration	Start	Finish	Predecessors	Resource Names	28 Nov 21					
								S	M	T	W	T	
29		Vorbereiding brede wer...	7 days	2/18/22 8:30 AM	3/7/22 8:30 AM	20;27							
30		Brede werksessie 1: ops...	7 days?	3/7/22 8:30 AM	3/16/22 8:30 AM	28;29	Prolander: communicatie						
31		Opstellen cVO	7 days?	3/16/22 8:30 AM	3/25/22 8:30 AM	30							
32		Vergunningen scan	7 days?	3/16/22 8:30 AM	3/25/22 8:30 AM	30							
33		Actualisatie gebiedsplan	7 days?	3/16/22 8:30 AM	3/25/22 8:30 AM	30							
34		Gesprekken gebiedspart...	14 days	3/25/22 8:30 AM	4/14/22 8:30 AM	30;33	Prolander						
35		Must haves definitief	7 days?	4/14/22 8:30 AM	4/25/22 8:30 AM	34							
36		Vorbereiding brede wer...	1 day?	4/25/22 8:30 AM	4/26/22 8:30 AM	35	Prolander: input voor aanpak						
37		Brede werksessie 2: pre...	1 day?	4/26/22 8:30 AM	4/27/22 8:30 AM	31;36	Prolander: communicatie						
38		SSK raming gebaseerd o...	7 days	4/26/22 8:30 AM	5/9/22 8:30 AM	36							
39		Presentatie programmat...	1 day?	5/9/22 8:30 AM	5/10/22 8:30 AM	38							
40		Presentatie bestuurlijke ...	1 day?	5/10/22 8:30 AM	5/11/22 8:30 AM	39	Prolander: data						
41		Informatieavond streek	1 day?	5/11/22 8:30 AM	5/12/22 8:30 AM	40	Prolander						
42		Versturen reactienota	1 day?	5/12/22 8:30 AM	5/13/22 8:30 AM	41	Prolander						
43		Opstellen concept vergu...	14 days	5/13/22 8:30 AM	6/2/22 8:30 AM	42							
44		Opstellen concept beste...	14 days	5/12/22 8:30 AM	6/1/22 8:30 AM	41							
45		Afrondende sessie fase 2	7 days?	6/1/22 8:30 AM	6/10/22 8:30 AM	44							
46		<b>Fase 3: DO</b>	<b>40 days?</b>	<b>6/10/22 8:30 AM</b>	<b>9/14/22 8:30 AM</b>	<b>45</b>							
47		GIS DO plankkaart met ta...	7 days	6/10/22 8:30 AM	6/21/22 8:30 AM	45							
48		Vaststellen DO (incl EBO)	1 day?	6/21/22 8:30 AM	6/22/22 8:30 AM	47							
49		Definitief maken vergun...	1 day?	6/22/22 8:30 AM	6/23/22 8:30 AM	47;48							
50		Formele procedure verg...	30 days	6/23/22 8:30 AM	9/13/22 8:30 AM	49							
51		Presentatie EBO DO plan...	1 day?	6/22/22 8:30 AM	6/23/22 8:30 AM	48	Prolander						
52		Eindoverleg	1 day?	9/13/22 8:30 AM	9/14/22 8:30 AM	51;50							
54		<b>Projectmanagement</b>	<b>195 days</b>	<b>12/14/21 8:30 AM</b>	<b>11/11/22 8:30 AM</b>								
55		<b>regulier intern overleg</b>	<b>188 days</b>	<b>12/14/21 8:30 AM</b>	<b>11/2/22 8:30 AM</b>								
56		regulier intern overleg 1	1 day	12/14/21 8:30 AM	12/15/21 8:30 AM								
57		regulier intern overleg 2	1 day	12/28/21 8:30 AM	12/29/21 8:30 AM								



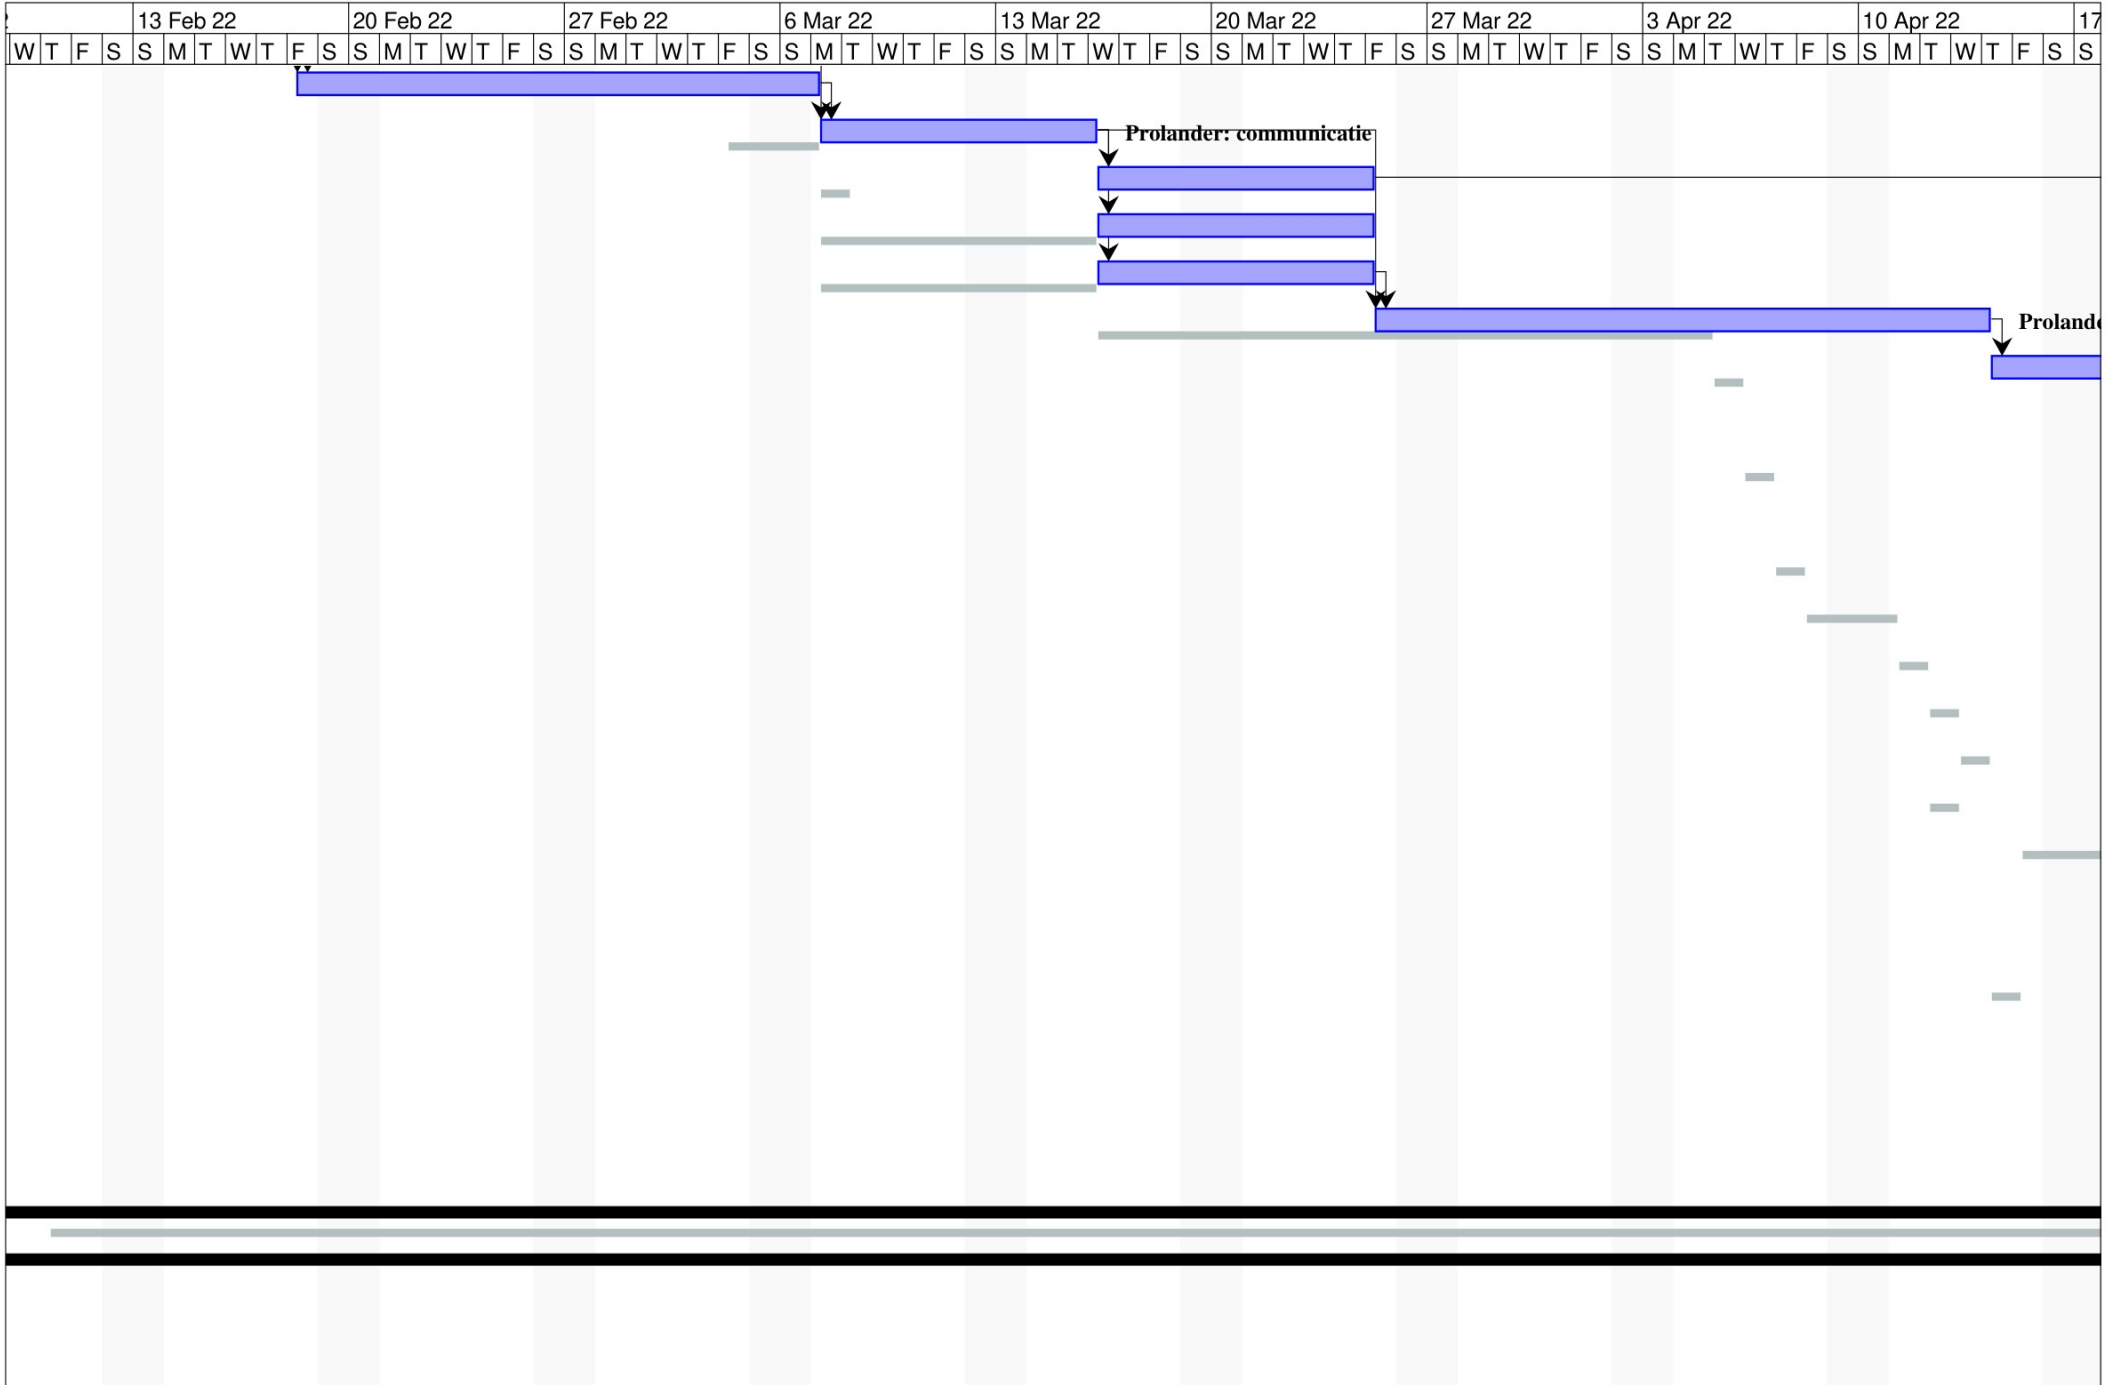

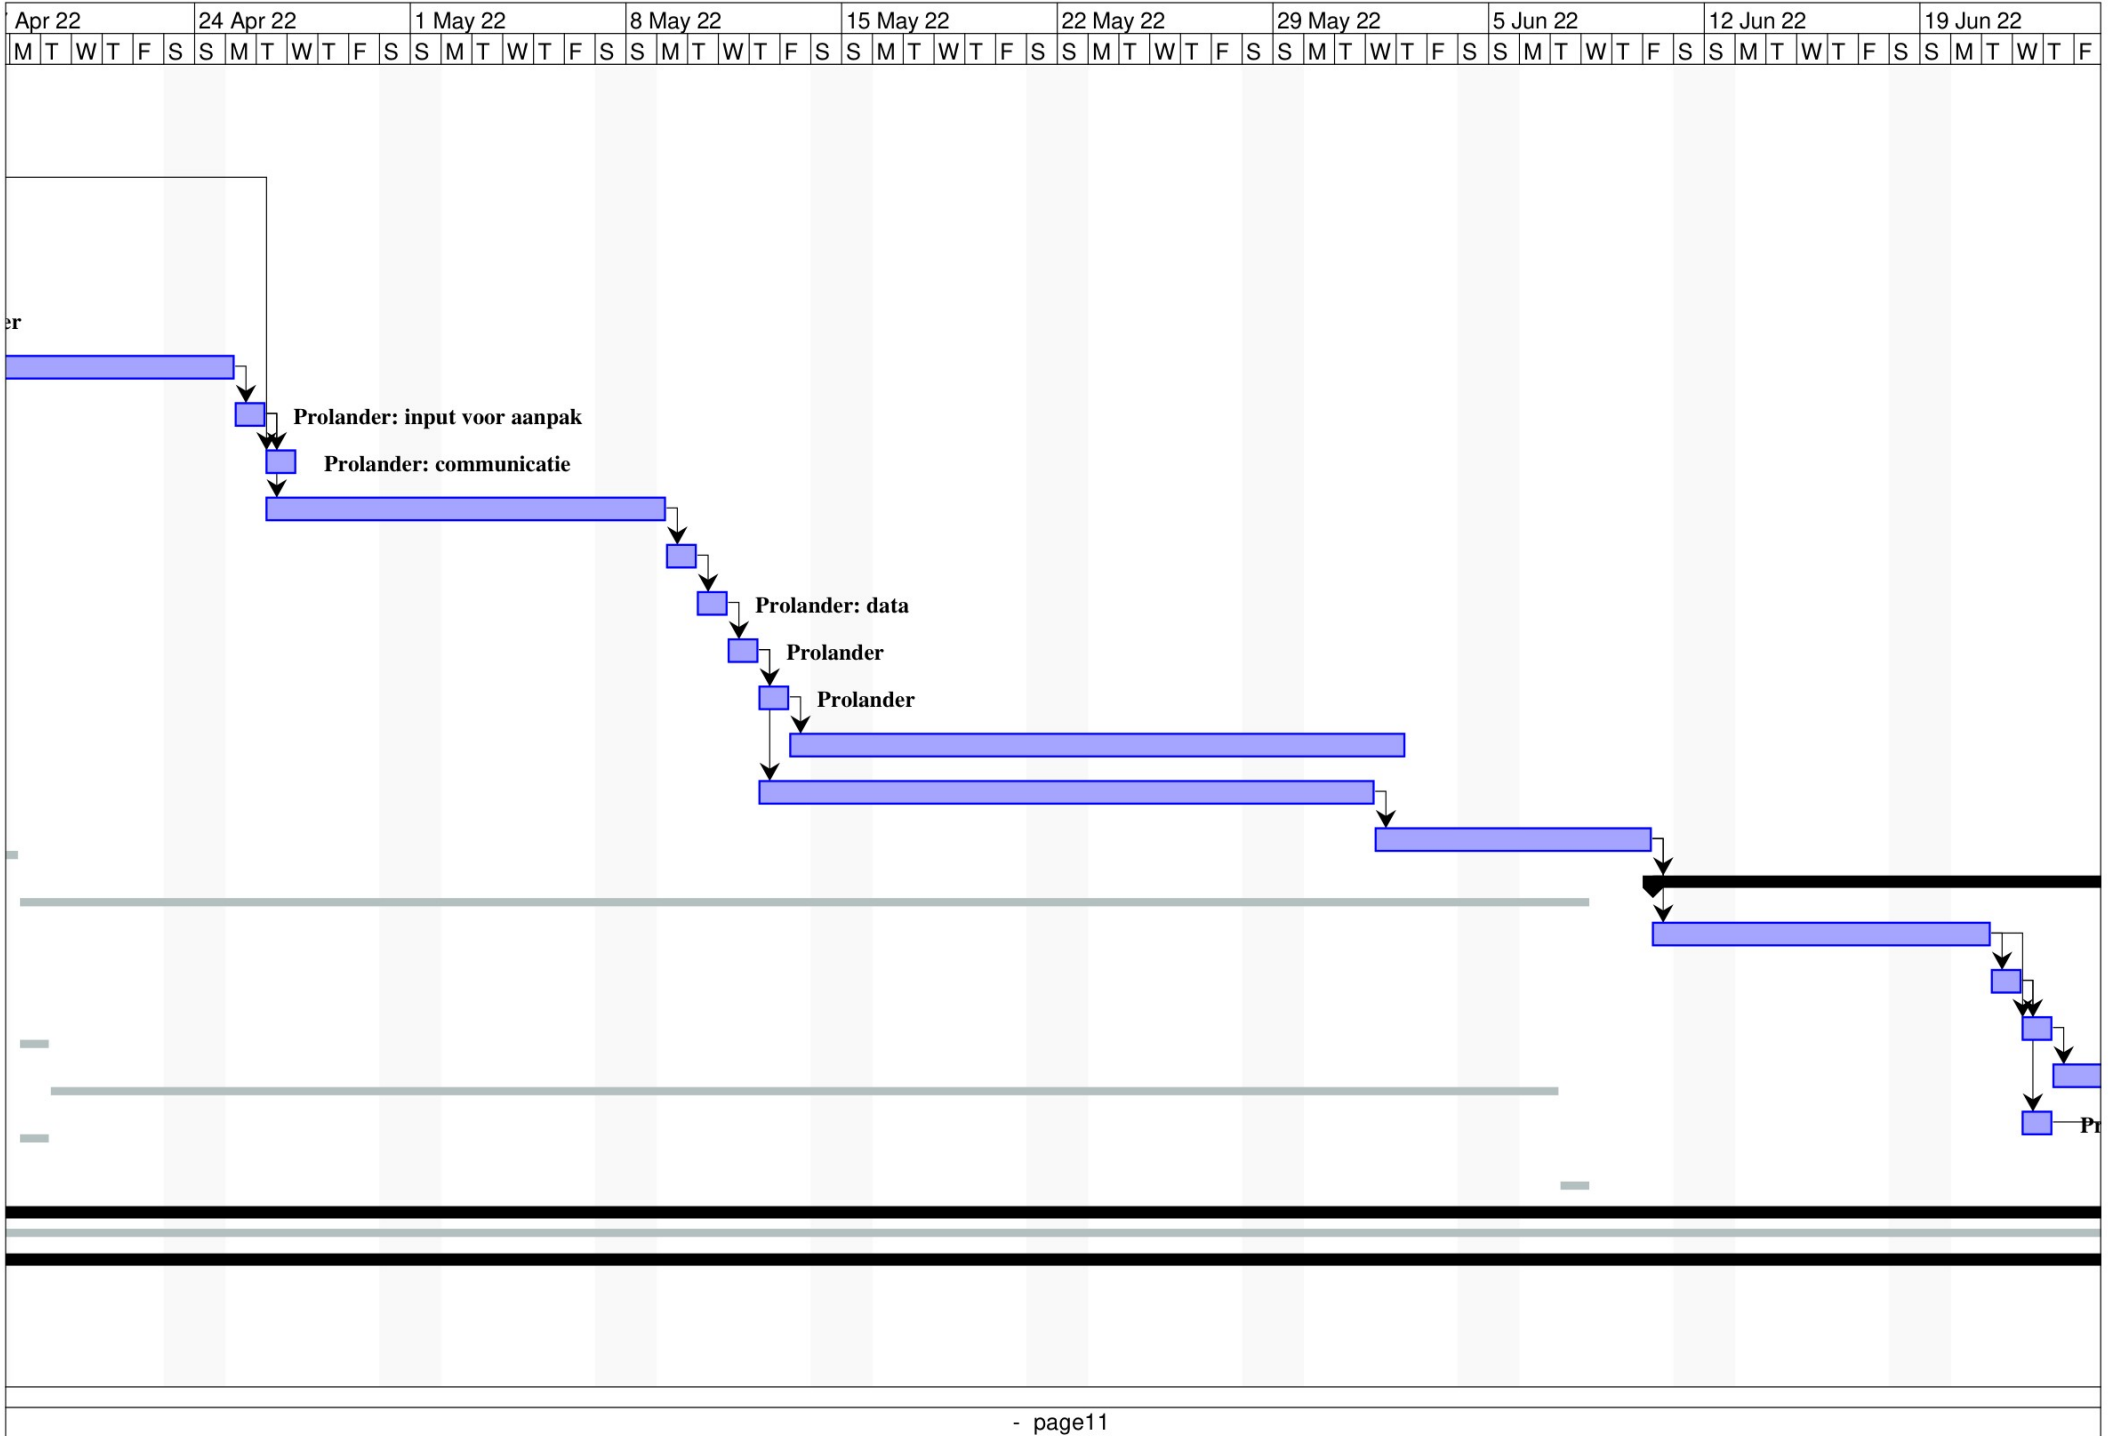





7 22				13 Nov 22				20 Nov 22				27 Nov 22				4 Dec 22				11						
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S



		Name	Duration	Start	Finish	Predecessors	Resource Names	28 Nov 21			
								S	M	T	W
58		regulier intern overleg 3	1 day	1/11/22 8:30 AM	1/12/22 8:30 AM						
59		regulier intern overleg 4	1 day	1/25/22 8:30 AM	1/26/22 8:30 AM						
60		regulier intern overleg 5	1 day	2/8/22 8:30 AM	2/9/22 8:30 AM						
61		regulier intern overleg 6	1 day	2/22/22 8:30 AM	2/23/22 8:30 AM						
62		regulier intern overleg 7	1 day	3/8/22 8:30 AM	3/9/22 8:30 AM						
63		regulier intern overleg 8	1 day	3/22/22 8:30 AM	3/23/22 8:30 AM						
64		regulier intern overleg 9	1 day	4/5/22 8:30 AM	4/6/22 8:30 AM						
65		regulier intern overleg 10	1 day	4/19/22 8:30 AM	4/20/22 8:30 AM						
66		regulier intern overleg 11	1 day	5/3/22 8:30 AM	5/4/22 8:30 AM						
67		regulier intern overleg 12	1 day	5/17/22 8:30 AM	5/18/22 8:30 AM						
68		regulier intern overleg 13	1 day	5/31/22 8:30 AM	6/1/22 8:30 AM						
69		regulier intern overleg 14	1 day	6/14/22 8:30 AM	6/15/22 8:30 AM						
70		regulier intern overleg 15	1 day	6/28/22 8:30 AM	6/29/22 8:30 AM						
71		regulier intern overleg 16	1 day	7/12/22 8:30 AM	7/13/22 8:30 AM						
72		regulier intern overleg 17	1 day	7/26/22 8:30 AM	7/27/22 8:30 AM						
73		regulier intern overleg 18	1 day	8/9/22 8:30 AM	8/10/22 8:30 AM						
74		regulier intern overleg 19	1 day	8/23/22 8:30 AM	8/24/22 8:30 AM						
75		regulier intern overleg 20	1 day	9/6/22 8:30 AM	9/7/22 8:30 AM						
76		regulier intern overleg 21	1 day	9/20/22 8:30 AM	9/21/22 8:30 AM						
77		regulier intern overleg 22	1 day	10/4/22 8:30 AM	10/5/22 8:30 AM						
78		regulier intern overleg 23	1 day	10/18/22 8:30 AM	10/19/22 8:30 AM						
79		regulier intern overleg 24	1 day	11/1/22 8:30 AM	11/2/22 8:30 AM						
80		<b>Regulier projectoverl...</b>	<b>160 days</b>	<b>2/10/22 8:30 AM</b>	<b>11/11/22 8:30 AM</b>						
81		Regulier projectoverleg 1	1 day	2/10/22 8:30 AM	2/11/22 8:30 AM						
82		Regulier projectoverleg 2	1 day	3/10/22 8:30 AM	3/11/22 8:30 AM						
83		Regulier projectoverleg 3	1 day	4/10/22 8:30 AM	4/11/22 5:00 PM						
84		Regulier projectoverleg 4	1 day	5/10/22 8:30 AM	5/11/22 8:30 AM						
85		Regulier projectoverleg 5	1 day	6/10/22 8:30 AM	6/13/22 8:30 AM						


















7 22				13 Nov 22				20 Nov 22				27 Nov 22				4 Dec 22				11						
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S



		Name	Duration	Start	Finish	Predecessors	Resource Names	28 Nov 21				
								S	M	T	W	T
86		Regulier projectoverleg 6	1 day	7/10/22 8:30 AM	7/11/22 5:00 PM							
87		Regulier projectoverleg 7	1 day	8/10/22 8:30 AM	8/11/22 8:30 AM							
88		Regulier projectoverleg 8	1 day	9/10/22 8:30 AM	9/12/22 5:00 PM							
89		Regulier projectoverleg 9	1 day	10/10/22 8:30 AM	10/11/22 8:30 AM							
90		Regulier projectoverle...	1 day	11/10/22 8:30 AM	11/11/22 8:30 AM							
187			1 day?	12/1/21 8:30 AM	12/2/21 8:30 AM							





Apr 22					24 Apr 22					1 May 22					8 May 22					15 May 22					22 May 22					29 May 22					5 Jun 22					12 Jun 22					19 Jun 22																							
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S							





7 22				13 Nov 22				20 Nov 22				27 Nov 22				4 Dec 22				11						
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
